



Quality Assurance Site Survey Report for Van Nuys Airport

Last updated March 2010

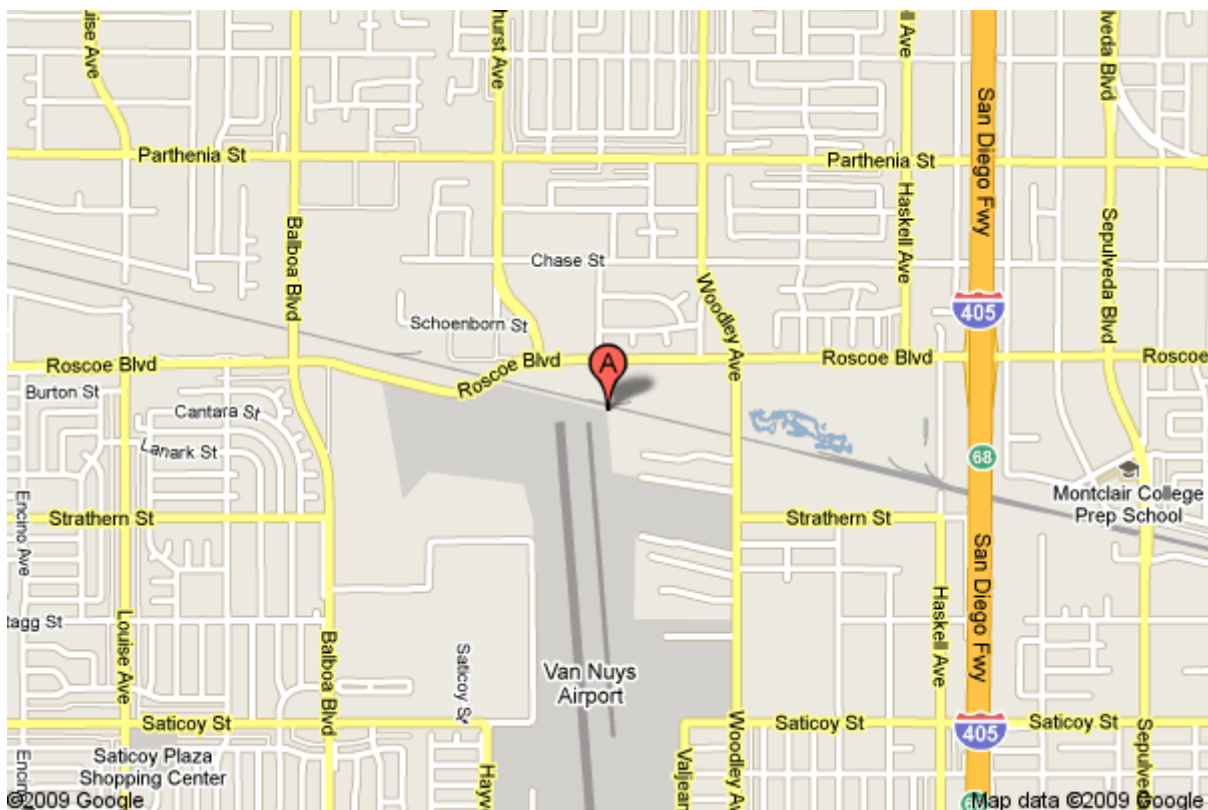

AIRS Number	ARB Number	Site Start Date	Reporting Agency and Agency Code
060371402	70041	1/1/10	South Coast AQMD (061)

Site Address	County	Air Basin	Latitude	Longitude	Elevation
16345 Raymer (Lot A) Van Nuys CA, 91406-1212	Los Angeles	South Coast	34° 13' 10"	-118° 29' 21"	244 m

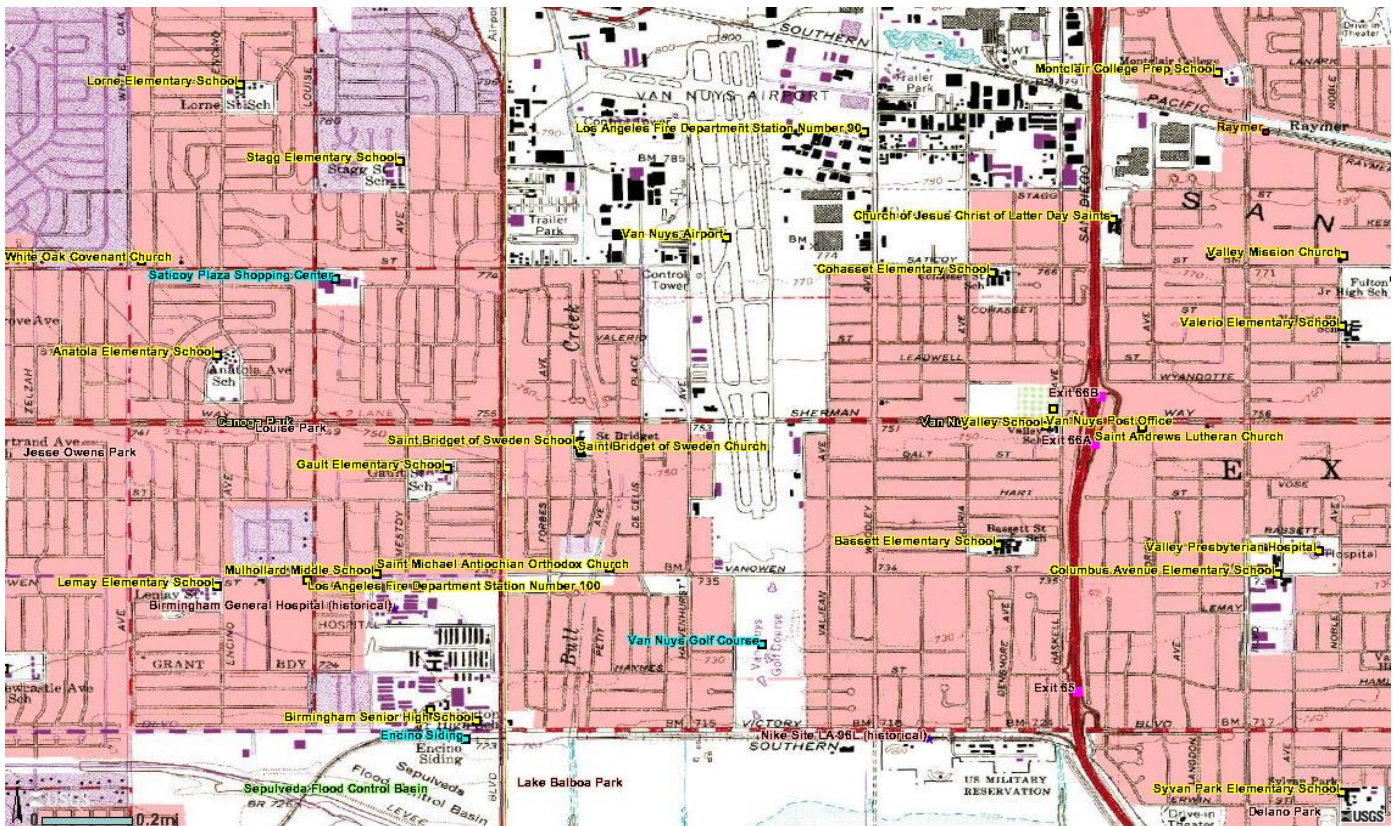

Site Survey Report

Siting Information

Site Name: Van Nuys A.P.	Date: 03/02/10	State Code: NA	AIRS Number: 060371402
Address: 16345 Raymer (Lot A) Van Nuys CA, 91406-1212	Latitude: 34° 13' 10"	Longitude: -118° 29' 21"	Elevation (m): 244 m
	Senior AQIS: Albert Dietrich	Site Technician: Norm Broellos	Site Phone: N/A
Operating Agency: South Coast AQMD			

General Siting Conditions

Station Temperature Controlled: No Recorded: No	Traffic Description: Commercial Distance: 520m Count 30,882	Topography Site: Level Region: Level	Predominant Wind Direction: NNW
			Arc Air Flow (Deg): 360
			Probe Last Cleaned Date: N/A
Meteorology Located With Instruments: No	Non-vehicular Local Sources Description: Airplane Distance: 30m Direction: South West	QA Manual	Manifold Clean: N/A
		Approved: Yes	Cleaning Schedule: N/A
		Agency: South Coast AQMD	Autocalibrator Type: N/A
		Urbanization: Urban	Site Survey Complete: Yes
		Ground Cover: Dirt / Asphalt	Logbook Up To Date: Yes

Action Items

--

Comments

--

Detailed Site Information

Site Name	Van Nuys Airport			
AQS ID (AIRS #)	060371402			
GIS coordinates	Latitude: 34° 13' 10" Longitude: -118° 29' 21"			
Location	Commercial			
Address	16345 Raymer (Lot A) Van Nuys CA, 91406-1212			
County	Los Angeles			
Dist. to road	520m (Roscoe Blvd \ Woodley Ave.)			
Traffic count	30,882			
Groundcover	Dirt/Asphalt			
Representative Area	31100-Los Angeles-Long Beach-Santa Ana			
Pollutant	TSP			
Monitor obj	Source Impact			
Spatial scale	Microscale			
Sampling method	GMW TSP			
Serial #	1561			
Property #	53354			
Last Calibration Date	1/1/10			
Analysis method	Inductively Coupled Argon Plasma-Mass Spectrometry			
Start date	1/1/10			
Operation schedule	1:6			
Sampling season	All Year			
Probe height	2.6			
Distance from supporting structure	N/A			
Distance from obstructions on roof	N/A			
Distance from obstructions not on roof	N/A			
Distance from trees	N/A			
Distance to furnace or incinerator flue	N/A			
Distance between collocated monitors	N/A			
Unrestricted airflow	Yes			
Probe material	N/A			
Residence time	N/A			
Will there be changes within the next 18 months?	No			
Is it suitable for comparison against the annual PM2.5?	N/A			
Frequency of flow rate verification for manual PM samplers audit	N/A			

Air Quality Monitoring Network Plan – July 2010

Frequency of flow rate verification for automated PM analyzers audit	N/A			
Frequency of one-point QC check (gaseous)	N/A			


**Van Nuys Airport
Site Photos**



Looking North toward probe



Looking East from the probe.

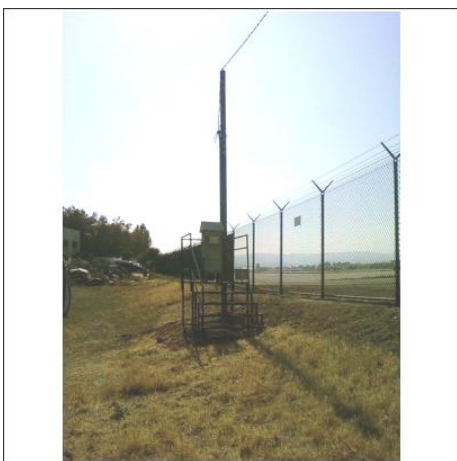

Looking South toward the probe.



Looking West toward the probe
